

**NOTES**


- EXISTING CONDITIONS DEPICTED ON THIS PLAN HAVE BEEN TAKEN FROM SURVEYS PREPARED BY BADEY & WATSON, SURVEYING AND ENGINEERING, P.C.
- THIS PLAN IS FOR TEMPORARY EROSION AND SEDIMENT CONTROL INFORMATION ONLY.
- PRIOR TO BEGINNING ANY CLEARING, GRUBBING OR EXCAVATION, ALL EROSION AND SEDIMENT CONTROL MEASURES SHALL BE INSTALLED IN ACCORDANCE WITH ALL THE PLANS AND SPECIFICATIONS FOR EROSION AND SEDIMENT CONTROL MEASURES SHALL BE MAINTAINED UNTIL THE SITE IS STABILIZED, FINAL STABILIZATION OF LANDSCAPED AREAS SHALL BE IN ACCORDANCE WITH THE LANDSCAPE PLAN.
- THE CONTRACTOR SHALL INSPECT AND MAINTAIN ON-SITE EROSION AND SEDIMENT CONTROL MEASURES ON A DAILY BASIS. ALL COLLECTED SEDIMENT WITHIN SEDIMENT BARRIERS SHALL BE REMOVED PERIODICALLY AS REQUIRED TO MAINTAIN THE FUNCTION OF THE SEDIMENT BARRIERS. ALL SEDIMENT COLLECTED SHALL BE RESPIRED ON-SITE WITH STABILIZED AREAS AS DIRECTED BY THE OWNER'S REPRESENTATIVE.
- THE CONTRACTOR SHALL INSPECT DOWNSTREAM CONDITIONS FOR EVIDENCE OF SEDIMENTATION ON A WEEKLY BASIS, AFTER EACH RAINSTORM, AND AS MAY BE REQUIRED OR DIRECTED BY ALL APPLICABLE APPROVALS AND PERMITS. THE CONTRACTOR SHALL IMMEDIATELY PROVIDE A WRITTEN REPORT ON FINDINGS OF SEDIMENT IN DOWNSTREAM AREAS TO ALL AUTHORITIES HAVING JURISDICTION AND MAKE REPAIRS AS REQUIRED OR DIRECTED.
- ADDITIONAL EROSION AND SEDIMENT CONTROL MEASURES SHALL BE INSTALLED BY THE CONTRACTOR AS REQUIRED/WARRANTED BY FIELD CONDITIONS AND AS DIRECTED BY THE OWNER'S REPRESENTATIVE, AEC, AND/OR ANY AUTHORITY HAVING JURISDICTION.
- STOCKPILING OF CONSTRUCTION MATERIAL SHALL BE PLACED ON-SITE IN THE AREA DESIGNATED ON THIS PLAN OR AS APPROVED BY THE OWNER'S REPRESENTATIVE. STOCKPILED EXCAVATED MATERIAL SHALL HAVE TWO ROWS OF SILT FENCE LOCATED AROUND ITS PERIMETER. ALL STOCKPILED MATERIAL SHALL BE MAINTAINED IN AN ORDERLY MANNER SO AS NOT TO IMPED EROSION AND/OR VEHICULAR TRAFFIC CIRCULATION ROUTES.
- DUST SHALL BE CONTROLLED BY SPRINKLING OR OTHER APPROVED METHODS AS NECESSARY, OR AS DIRECTED BY THE OWNER'S REPRESENTATIVE.
- ALL EXPOSED SOLES AND GRASS/RESURFACED AREAS THAT WILL NOT BE FURTHER DISTURBED WITHIN 14 CALENDAR DAYS (7 DAYS FOR CONSTRUCTION SITES THAT EITHER DIRECTLY DISCHARGE TO ONE OF THE 3000+ STREAMS LISTED IN APPENDIX E OF THE GENERAL PERMIT OR ARE LOCATED WITHIN ONE OF THE WATERSHEDS LISTED IN APPENDIX C OF THE GENERAL PERMIT), SHALL BE TEMPORARILY SEEDED WITHIN 24 HOURS OF DISTURBANCE, IN ACCORDANCE WITH THE NEW YORK STATE DEPARTMENT OF ENVIRONMENTAL CONSERVATION (NYSDEC) "EROSION AND SEDIMENT CONTROL GUIDELINES" AND THE ALSO "BEST MANAGEMENT PRACTICES FOR TREE AND SHRUB PLANTING, TRANSPLANTING, MAINTENANCE AND CARE" PREPARED BY THE INTERNATIONAL SOCIETY OF ARBORICULTURE (ISA), LATEST EDITIONS, AS FOLLOWS:
  - SEED MIXTURE AND RATE OF APPLICATION
  - IN SPRING, SUMMER OR EARLY FALL, SEED THE AREA WITH HYDRASS (ANNUAL OR PERENNIAL) AT 30 POUNDS PER ACRE (APPROXIMATELY 17 POUNDS/1000 SQUARE FEET) OR USE 1 POUND/1000 SQUARE FEET.
  - IN LATE FALL OR EARLY WINTER, SEED THE AREA WITH CERTIFIED "ARBORETUM" WINTER WHE (CERIAL WHE) AT 100 POUNDS PER ACRE (2.5 POUNDS/1000 SQUARE FEET).
  - APPLICATION SHALL BE UNIFORM BY MECHANICAL OR HYDROSEED METHODS.
  - MULCH ALL SEEDED AREAS WITH STRAW AT A RATE OF 2 TONS PER ACRE (50 POUNDS PER 1000 SQUARE FEET) SUCH THAT THE MULCH FORMS A CONTINUOUS BLANKET.
  - ALL SEEDING AREAS SHALL BE FERTILIZED, RESEEDED, AND MACHED AS NECESSARY TO MAINTAIN WOODED, DENSE VEGETATIVE COVER.
  - TEMPORARY SEED MIXTURES SHALL NOT BE PLACED ON AREAS WHERE FINAL GRADE HAS BEEN ESTABLISHED AND TOPSOIL HAS BEEN PLACED UNLESS OTHERWISE DIRECTED BY THE PROJECT LANDSCAPE ARCHITECT.

**SEQUENCE OF CONSTRUCTION**



- DEMOLITION OF EXISTING BUILDINGS AS REQUIRED.
- INSTALLATION OF SEDIMENT AND EROSION CONTROL MEASURES AS INDICATED ON THIS PLAN.
- CLEAR UNDEVELOPED PORTION OF PROPERTY WHICH IS TO BE DEVELOPED.
- STRIP AND STOODPLE TOPSOIL.
- BEGIN BUILDING AND PARKING LOT CONSTRUCTION, ROUGH GRADING.
- INSTALL STORM DRAIN SYSTEM COMPLETE (IMMEDIATELY INSTALL HARABLE FILTERS ON ALL INLETS).
- INSTALL PUBLIC UTILITIES (GAS, ELECTRIC AND TELEPHONE) AS REQUIRED.
- INSTALL CONCRETE AND ASPHALT CONCRETE PAVEMENT COMPLETE.
- FINISH GRADING, REDISTRIBUTE TOPSOIL AND ESTABLISH VEGETATION AND/OR LANDSCAPING.
- CLEAN PAVEMENTS AND STORM DRAIN SYSTEM OF ALL ACCUMULATED SEDIMENT IN CONJUNCTION WITH THE REMOVAL OF ALL TEMPORARY SEDIMENT AND EROSION CONTROL DEVICES.
- COMPLETE SITE AND BUILDING CONSTRUCTION.

**LEGEND**

- PROPOSED INLET PROTECTION
- PROPOSED CONSTRUCTION FENCE
- PROPOSED SILT FENCE
- PROPOSED LIMIT OF DISTURBANCE
- PROPOSED STABILIZED CONSTRUCTION ENTRANCE
- PROPOSED STOCKPILE AREA
- PROPOSED TEMPORARY SHALE
- PROPOSED TEMPORARY SEDIMENT BASIN
- TEMPORARY RISER & ANTI-VORTEX DEVICE
- EXISTING FEATURE TO BE REMOVED



**KEY MAP**  
SCALE: 1" = 1,500'

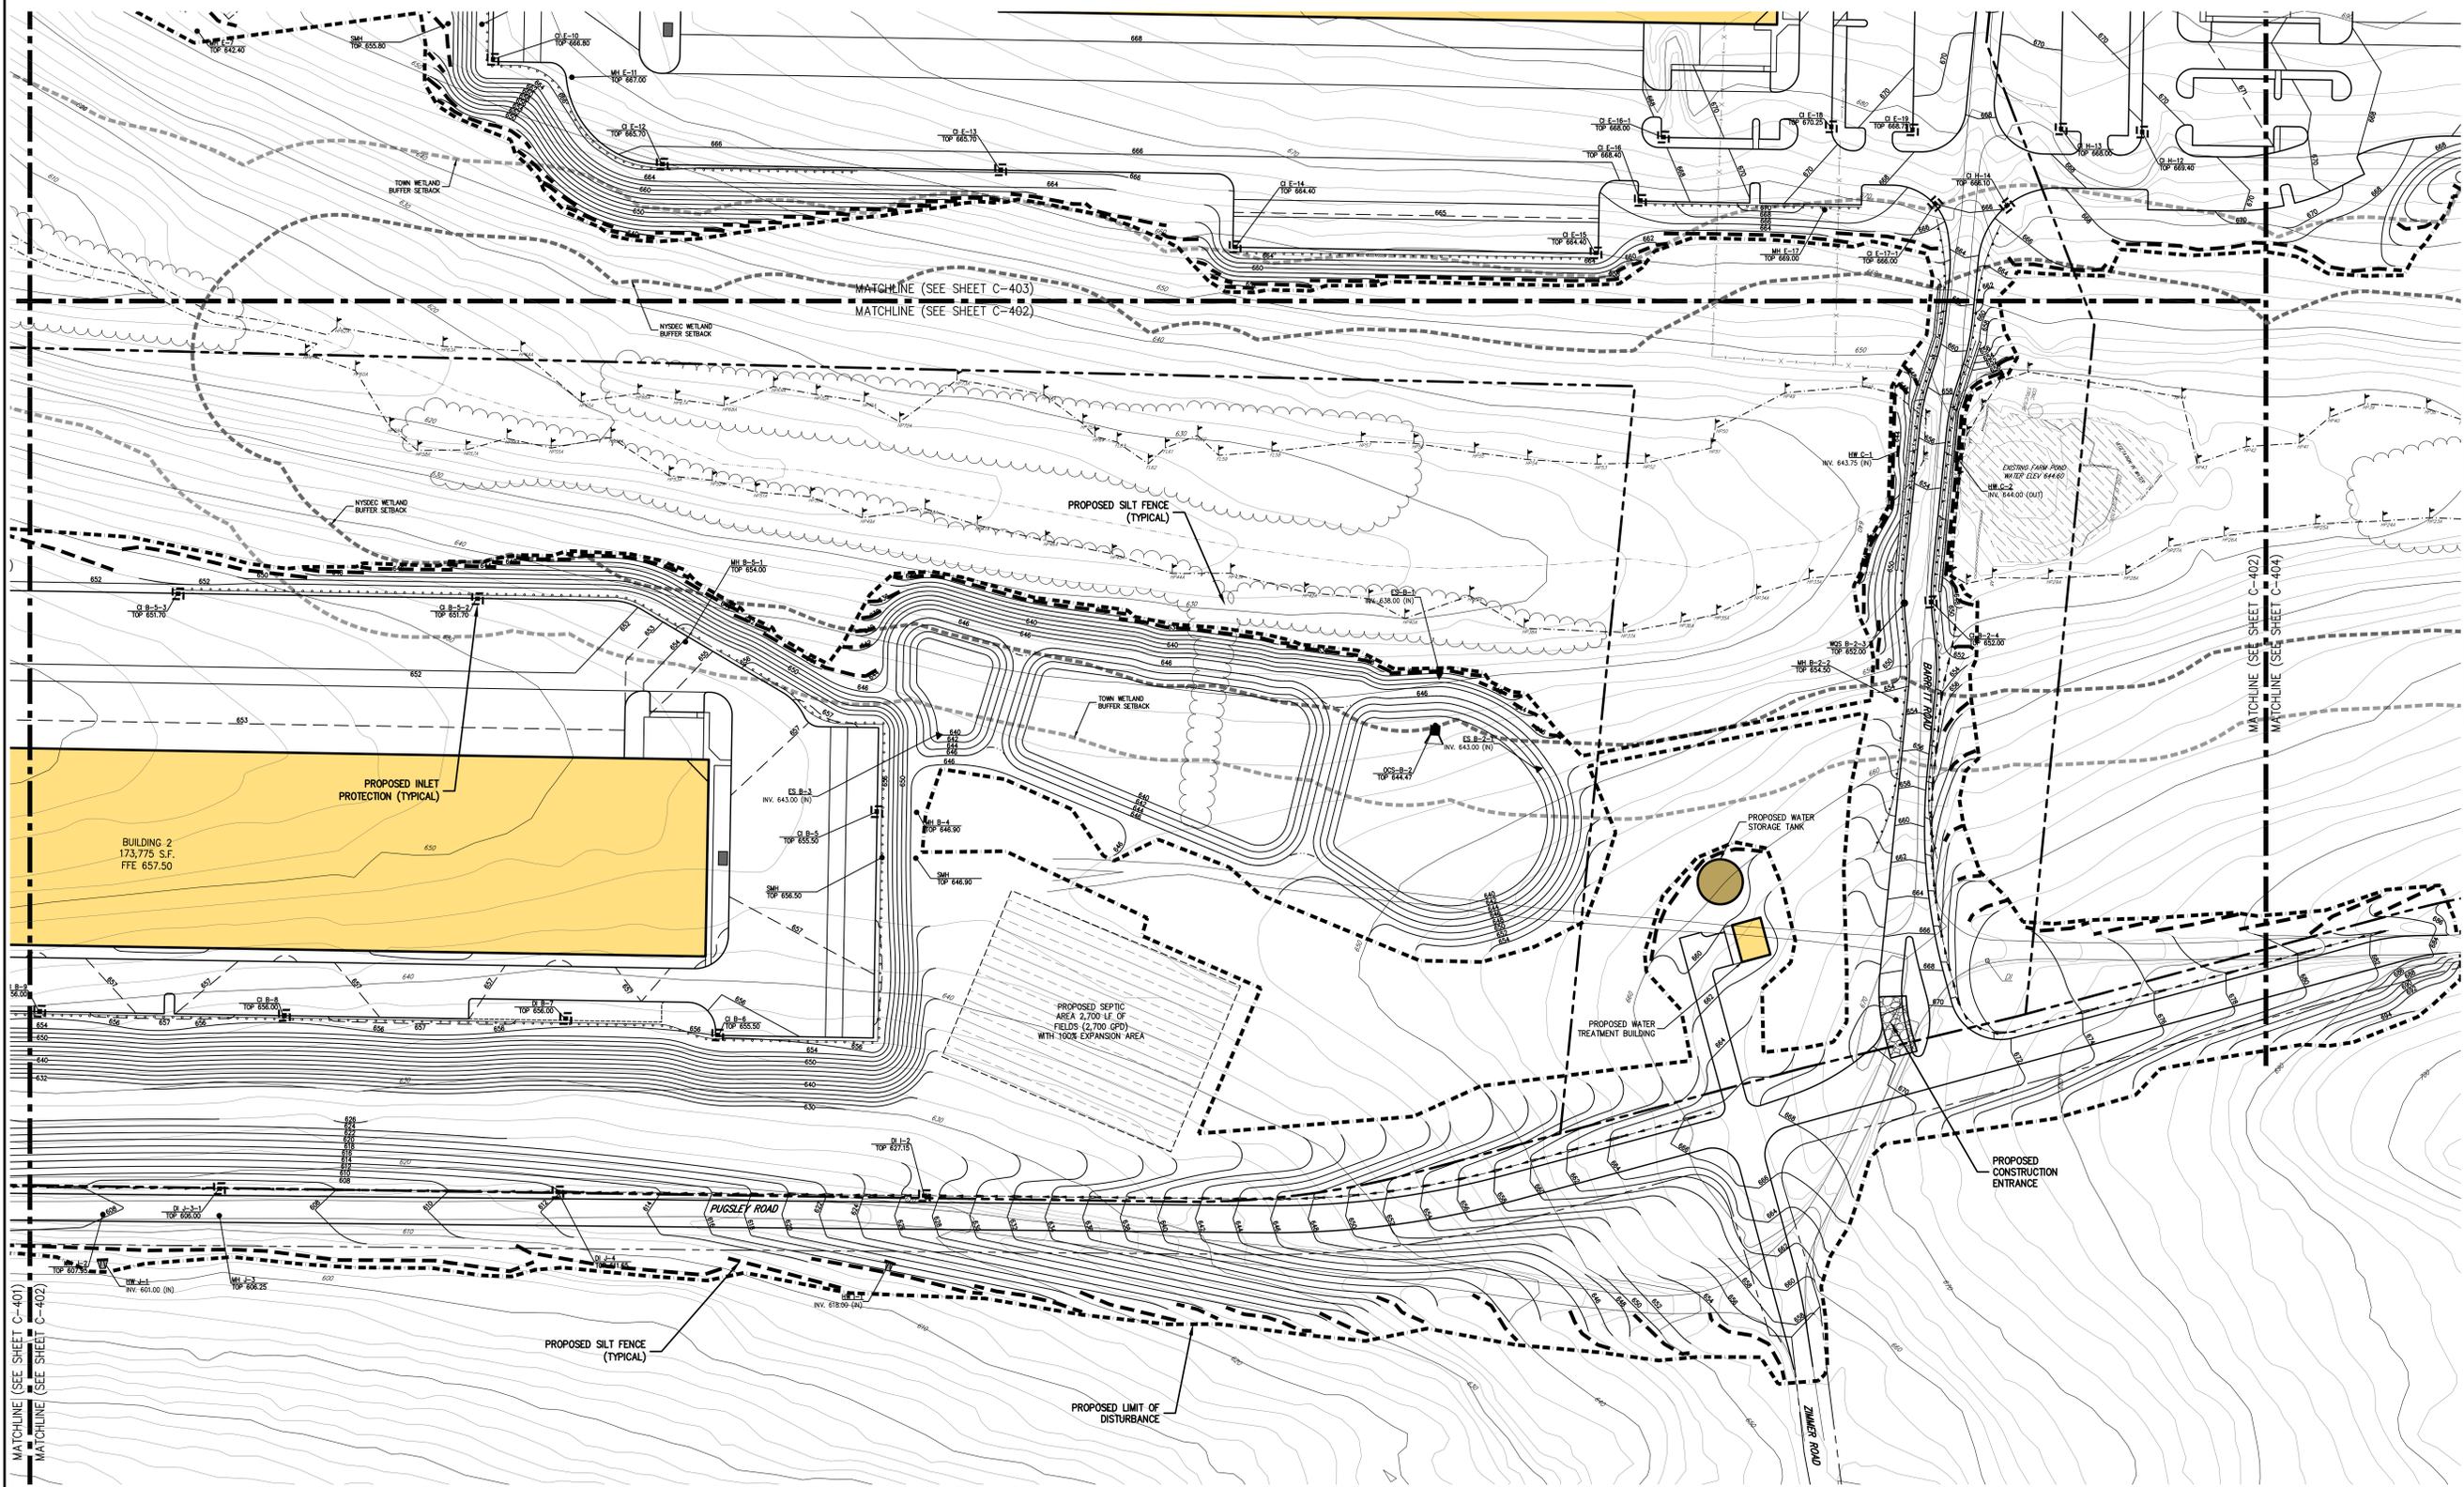

NOT FOR CONSTRUCTION

By	KRM
Date	05/11/2018
Revision	
No.	1
Description	DESS COMPLETION SUBMISSION

**PUTNAM SEABURY PARTNERS, L.P.**  
287 KING STREET  
CHAPPAQUA, NY 10514

JMC Planning, Engineering, Landscape Architecture & Land Surveying, LLC  
John Meyer Consulting, Inc.  
123 BEVERLY DR. - HARRISON, NY 10548  
PHONE: 914.333.5555 FAX: 914.333.4102  
www.jmcpllc.com



**EROSION & SEDIMENT CONTROL PLAN 'B'**  
NORTHEAST INTERSTATE LOGISTICS CENTER  
TOWN OF SOUTHEAST, NEW YORK

ANY ALTERATION OF PLANS, SPECIFICATIONS, PLATS AND REPORTS BEARING THE SEAL OF A LICENSED PROFESSIONAL ENGINEER OR LICENSED LAND SURVEYOR IS A VIOLATION OF SECTION 7209 OF THE NEW YORK STATE EDUCATION LAW, EXCEPT AS PROVIDED FOR BY SECTION 7209, SUBSECTION 2.

Drawn	KRM	Approved	R.P.
Scale	1" = 50'		
Date	11/06/2017		
Project No.	14012		
Sheet No.	SM B	of	4 SM sheets
Drawing No.			

**C-402**
