

LEGEND




	PROPOSED INLET PROTECTION
	PROPOSED CONSTRUCTION FENCE
	PROPOSED SILT FENCE
	PROPOSED LIMIT OF DISTURBANCE
	PROPOSED STABILIZED CONSTRUCTION ENTRANCE
	PROPOSED STOOPPLE AREA
	PROPOSED TEMPORARY SEALMENT
	PROPOSED TEMPORARY SEDIMENT BASIN
	PROPOSED TEMPORARY RISER & ANTI-VORTEX DEVICE
	EXISTING FEATURE TO BE REMOVED

SEQUENCE OF CONSTRUCTION

- CONSTRUCTION SHALL BE SEQUENCED IN SUCH A MANNER THAT ANY AREA WHICH IS DISTURBED SHALL BE PROTECTED WITH SEDIMENT EROSION CONTROL MEASURES AS INDICATED ON THIS PLAN. PARTICULAR REQUIREMENTS ARE GIVEN AS FOLLOWS:
- REMOVAL OF EXISTING BUILDINGS AS REQUIRED.
- INSTALLATION OF SEDIMENT AND EROSION CONTROL MEASURES AS INDICATED ON THIS PLAN.
- CLEAR UNDEVELOPED PORTION OF PROPERTY WHICH IS TO BE DEVELOPED.
- STRIP AND STOOPPLE TOPSOIL.
- BEgin BUILDING AND PARKING LOT CONSTRUCTION, ROUGH GRADING.
- INSTALL STORM DRAIN SYSTEM COMPLETE (IMMEDIATELY INSTALL HAYBALE FILTERS ON ALL INLETS).
- INSTALL PUBLIC UTILITIES (GAS, ELECTRIC AND TELEPHONE) AS REQUIRED.
- INSTALL CONCRETE AND ASPHALT CONCRETE PAVEMENT COMPLETE.
- FINISH GRADING, REDISTRIBUTE TOPSOIL AND ESTABLISH VEGETATION AND/OR LANDSCAPING.
- CLEAN PAVEMENTS AND STORM DRAIN SYSTEM OF ALL ACCUMULATED SEDIMENT IN CONNECTION WITH THE REMOVAL OF ALL TEMPORARY SEDIMENT AND EROSION CONTROL DEVICES.
- COMPLETE SITE AND BUILDING CONSTRUCTION.

NOTES

- EXISTING CONDITIONS SHOWN ON THIS PLAN HAVE BEEN TAKEN FROM SURVEYS PREPARED BY BACEY & WATSON, SURVEYING AND ENGINEERING, P.C.
- THIS PLAN IS FOR TEMPORARY EROSION AND SEDIMENT CONTROL INFORMATION ONLY.
- PRIOR TO BEGINNING ANY CLEARING, GRUBBING OR EXCAVATION, ALL EROSION AND SEDIMENT CONTROL MEASURES SHALL BE INSTALLED IN ACCORDANCE WITH ALL THE PLANS AND SPECIFICATIONS, EROSION AND SEDIMENT CONTROL MEASURES SHALL BE MAINTAINED UNTIL THE SITE IS STABILIZED. FINAL STABILIZATION OF LANDSCAPED AREAS SHALL BE IN ACCORDANCE WITH THE LANDSCAPE PLAN.
- THE CONTRACTOR SHALL INSPECT AND MAINTAIN ON-SITE EROSION AND SEDIMENT CONTROL MEASURES ON A DAILY BASIS. ALL COLLECTED SEDIMENT WITHIN SEDIMENT BARRIERS SHALL BE REMOVED PERIODICALLY AS REQUIRED TO MAINTAIN THE FUNCTION OF THE SEDIMENT BARRIERS. ALL SEDIMENT COLLECTED SHALL BE RESPAREAD ON-SITE WITH STABILIZED AREAS AS DIRECTED BY THE OWNER'S REPRESENTATIVE.
- THE CONTRACTOR SHALL INSPECT DOWNSTREAM CONDITIONS FOR EVIDENCE OF SEDIMENTATION ON A DAILY BASIS, AFTER EACH RAINFALL, AND AS MAY BE REQUIRED BY THE OWNER'S REPRESENTATIVE. APPROVAL AND PERMITS: THE CONTRACTOR SHALL IMMEDIATELY PROVIDE A WRITTEN REPORT ON FINDINGS OF SEDIMENT IN DOWNSTREAM AREAS TO ALL AUTHORITIES HAVING JURISDICTION AND MAKE REPAIRS AS REQUIRED OR DIRECTED.
- ADDITIONAL EROSION AND SEDIMENT CONTROL MEASURES SHALL BE INSTALLED BY THE CONTRACTOR AS REQUIRED/WARRANTED BY FIELD CONDITIONS AND AS DIRECTED BY THE OWNER'S REPRESENTATIVE, JMC, AND/OR ANY AUTHORITY HAVING JURISDICTION.
- STOPPING OF CONSTRUCTION MATERIAL SHALL BE PLACED ON-SITE IN THE AREA DESIGNATED ON THIS PLAN OR AS APPROVED BY THE OWNER'S REPRESENTATIVE. STOCKPILED EXCAVATED MATERIAL SHALL HAVE TWO ROWS OF SILT FENCE LOCATED AROUND ITS PERIMETER. ALL STOCKPILED MATERIAL SHALL BE MAINTAINED IN AN ORDERLY MANNER SO AS NOT TO IMPED ON PEDESTRIAN AND/OR VEHICULAR TRAFFIC CIRCULATION ROUTES.
- DUST SHALL BE CONTROLLED BY SPRINKLING OR OTHER APPROVED METHODS AS NECESSARY, OR AS DIRECTED BY THE OWNER'S REPRESENTATIVE.
- ALL EXPOSED SLOPES AND GRADED/DISTURBED AREAS THAT WILL NOT BE FURTHER DISTURBED WITHIN 14 CALENDAR DAYS (7 DAYS FOR CONSTRUCTION SITES THAT EITHER DIRECTLY DISCHARGE TO ONE OF THE 300(0) STREAMS LISTED IN APPENDIX E OF THE GENERAL PERMIT OR ARE LOCATED WITHIN ONE OF THE WATERSHEDS LISTED IN APPENDIX C OF THE GENERAL PERMIT), SHALL BE TEMPORARILY SEEDED WITHIN 24 HOURS OF DISTURBANCE. IN ACCORDANCE WITH THE NEW YORK STATE DEPARTMENT OF ENVIRONMENTAL CONSERVATION (NYSDEC) "EROSION AND SEDIMENT CONTROL GUIDANCE" AND THE AASD "BEST MANAGEMENT PRACTICES FOR TREE AND SHRUB PLANTING, TRANSPLANTING, MAINTENANCE AND CARE," PREPARED BY THE INTERNATIONAL SOCIETY OF ARBORICULTURE (ISA), LATEST EDITIONS, AS FOLLOWS:
 - SEED MIXTURE AND RATE OF APPLICATION
 - IN SPRING, SUMMER OR EARLY FALL, SEED THE AREA WITH HYDRASS (ANNUAL OR PERENNIAL) AT 30 POUNDS PER ACRE (APPROXIMATELY 0.17 POUNDS/1000 SQUARE FEET OR USE 1 POUND/1000 SQUARE FEET).
 - IN LATE FALL OR EARLY WINTER, SEED THE AREA WITH CERTIFIED "WOODSTOCK" WHEAT (THE GENERAL WHEAT) AT 100 POUNDS PER ACRE (2.5 POUNDS/1000 SQUARE FEET).
 - APPLICATION SHALL BE UNIFORM BY MECHANICAL OR HYDROSEED METHODS.
 - MULCH ALL SEEDED AREAS WITH STRAW AT A RATE OF 2 TONS PER ACRE (50 POUNDS PER 1000 SQUARE FEET) SUCH THAT THE MULCH FORMS A CONTINUOUS BARRIER.
 - ALL SEEDED AREAS SHALL BE FERTILIZED, WEEDKILLED AND MACHED AS NECESSARY TO MAINTAIN WOODED, DENSE VEGETATIVE COVER.
 - TEMPORARY SEED MIXTURES SHALL NOT BE PLACED ON AREAS WHERE FINAL GRADE HAS BEEN ESTABLISHED AND TOPSOIL HAS BEEN PLACED UNLESS OTHERWISE DIRECTED BY THE PROJECT LANDSCAPE ARCHITECT.

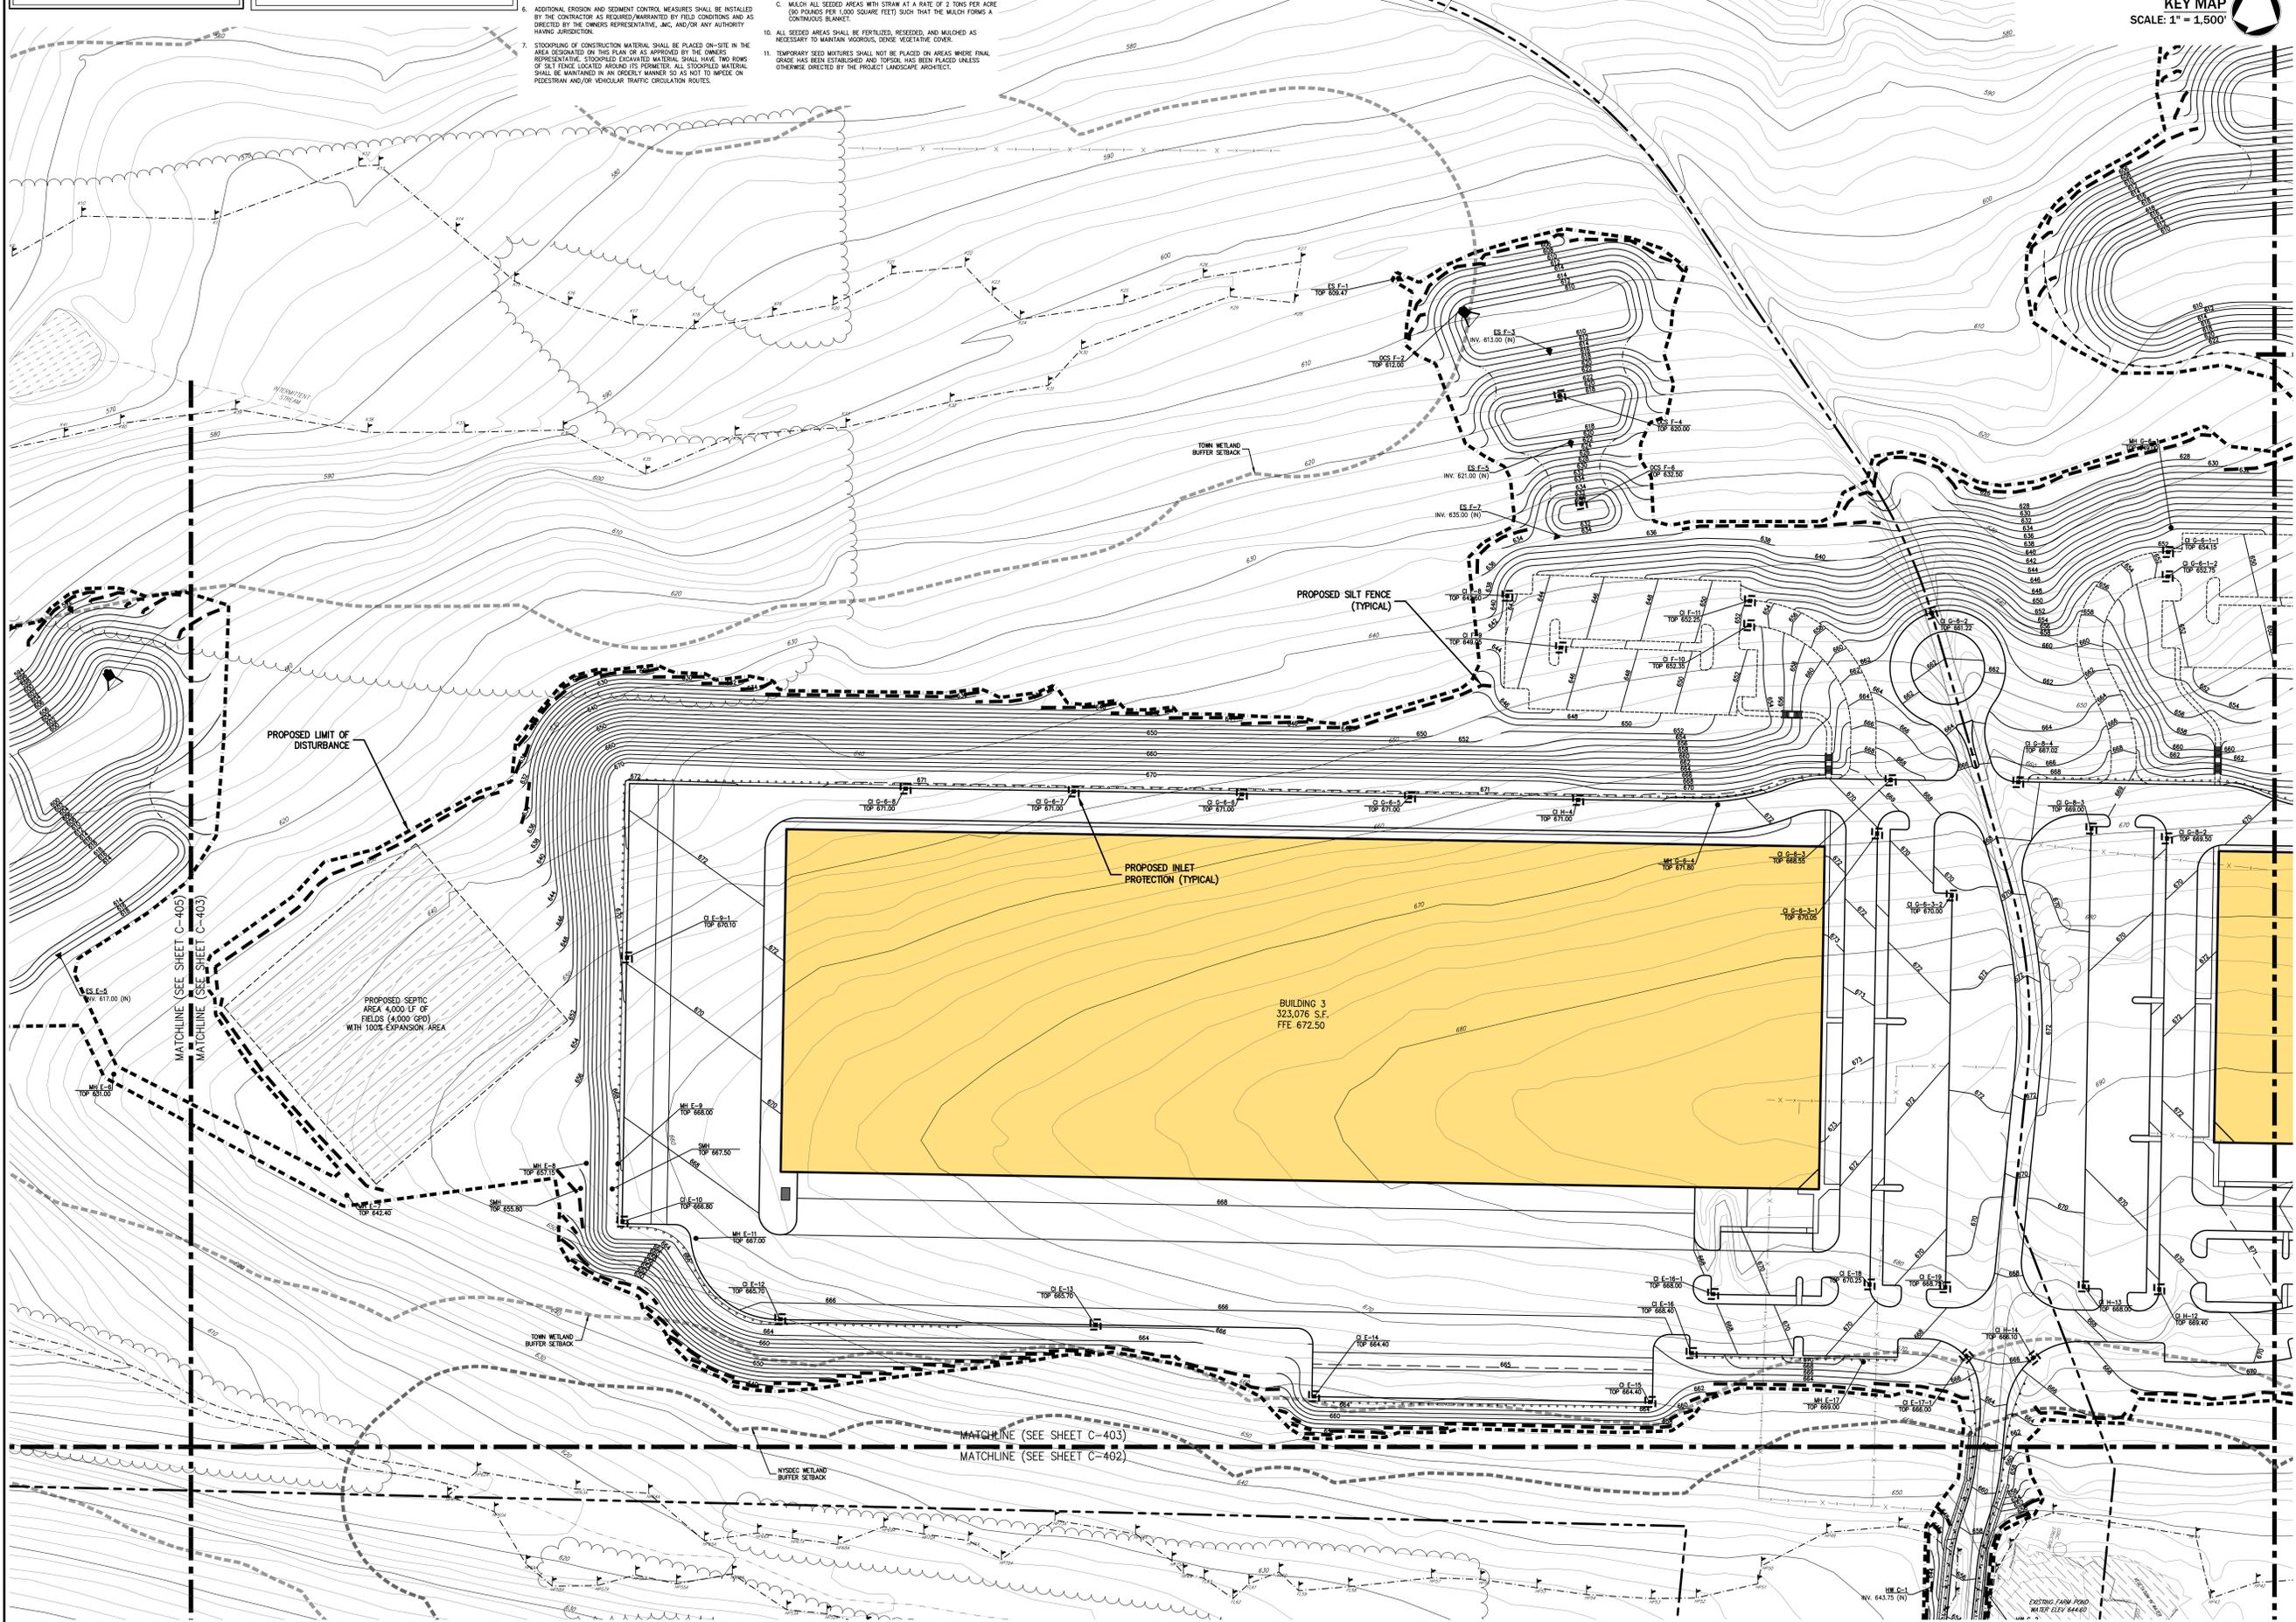

No.	1.	DATE	05/17/2018	BY	KRM
Revision	1. EBS COMPLETENESS SUBMISSION				

PUTNAM SEABURY PARTNERS, L.P.
287 KING STREET
CHAPPAQUA, NY 0514

JMC
JMC Planning, Engineering, Landscape Architecture & Land Surveying, LLC
John Meyer Consulting, Inc.
123 BEVERLY DR. - WARREN, NY 13554
PHONE: 518.533.5525 - FAX: 518.533.2102
www.jmcpllc.com



EROSION & SEDIMENT CONTROL PLAN 'C'
NORTHEAST INTERSTATE LOGISTICS CENTER
TOWN OF SOUTHEAST, NEW YORK

ANY ALTERATION OF PLANS, SPECIFICATIONS, PLATS AND REPORTS BEARING THE SEAL OF A LICENSED PROFESSIONAL ENGINEER OR LICENSED LAND SURVEYOR IS A VIOLATION OF SECTION 7209 OF THE NEW YORK STATE EDUCATION LAW, EXCEPT AS PROVIDED FOR BY SECTION 7209, SUBSECTION 2.

Drawn	KRM	Approved	R.P.
Scale	1" = 50'		
Date	11/06/2017		
Project No.	14012		
Sheet No.	SM C	of	4 SM C's
Checked	L.S.M.		
C-403			

NOT FOR CONSTRUCTION
